# Secure-Lock Drip Edge

METAL ROOFING SYSTEMS

WWW.METALROOFINGSYSTEMS.COM

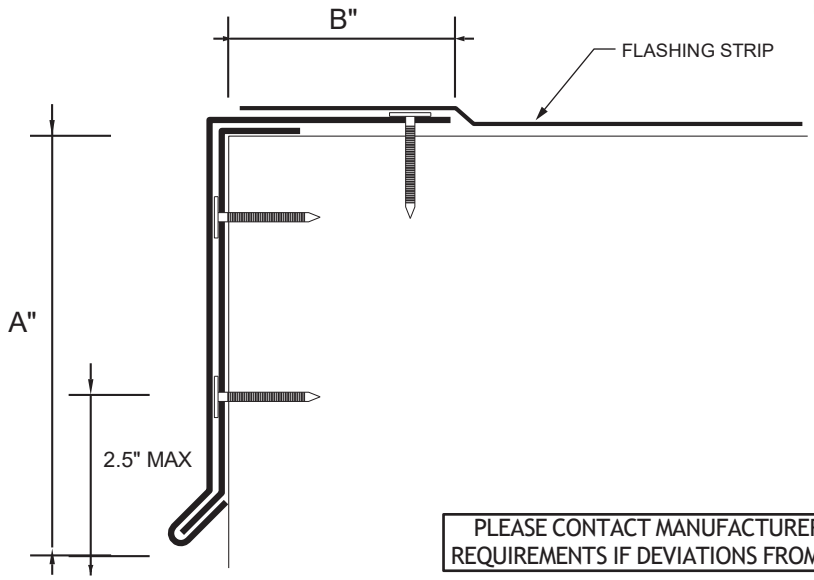


PLEASE CONTACT MANUFACTURER TO VERIFY ANSI SPRI ES-1 REQUIREMENTS IF DEVIATIONS FROM THE DESIGN ARE REQUIRED.

## DRIP EDGE DIMENSIONS

FRONT (A"): _____

TOP (B"): _____

## FINISH

KYNAR (painted) ☐

COLOR: _____

MILL FINISH (unfinished aluminum) ☐

GALVALUME (unfinished steel) ☐

## DRIP EDGE MATERIAL

24 GAUGE GALVALUME ☐

22 GAUGE GALVALUME ☐

.032 ALUMINUM ☐

.040 ALUMINUM ☐

.050 ALUMINUM ☐

.063 ALUMINUM ☐

## CLEAT MATERIAL

22 GAUGE GALVANIZED ☐

20 GAUGE GALVANIZED ☐

.050 ALUMINUM ☐

.063 ALUMINUM ☐

## PROJECT INFORMATION

PROJECT NAME: _____

PROJECT LOCATION: _____

BUILDING HEIGHT: _____

## CUSTOMER APPROVAL

ARCHITECT: _____

CUSTOMER: _____

AUTHOR SIGNATURE: _____

DATE: _____

## QUANTITY

*TOTAL LINEAR FEET: _____

INSIDE MITERS: _____

OUTSIDE MITERS: _____

END CAPS LEFT: _____ RIGHT: _____

END WALL TERMINATION LEFT: _____ RIGHT: _____

## NOTES

-UNLESS OTHERWISE NOTED, FABRICATION OF MITERS AND ACCESSORIES ARE FURNISHED WITH A NON-PENETRATING CLINCHED JOINT AND FACTORY APPLIED SEALANT.

-CHECK HERE IF WELDED MITERS AND ACCESSORIES ARE REQUIRED

☐ - REQUIRED (UPCHARGE)

- SYSTEM INCLUDES 6" WIDE CONCEALED SPLICE PLATES

# Secure-Lock Drip Edge

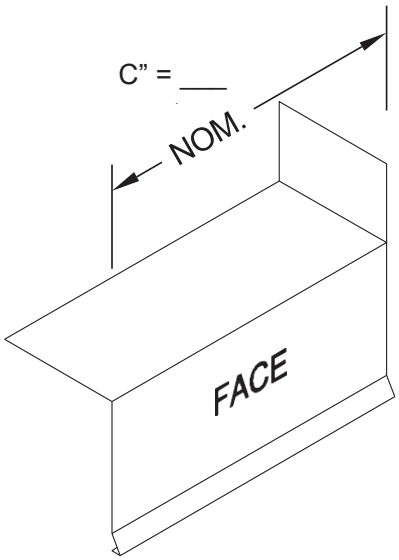


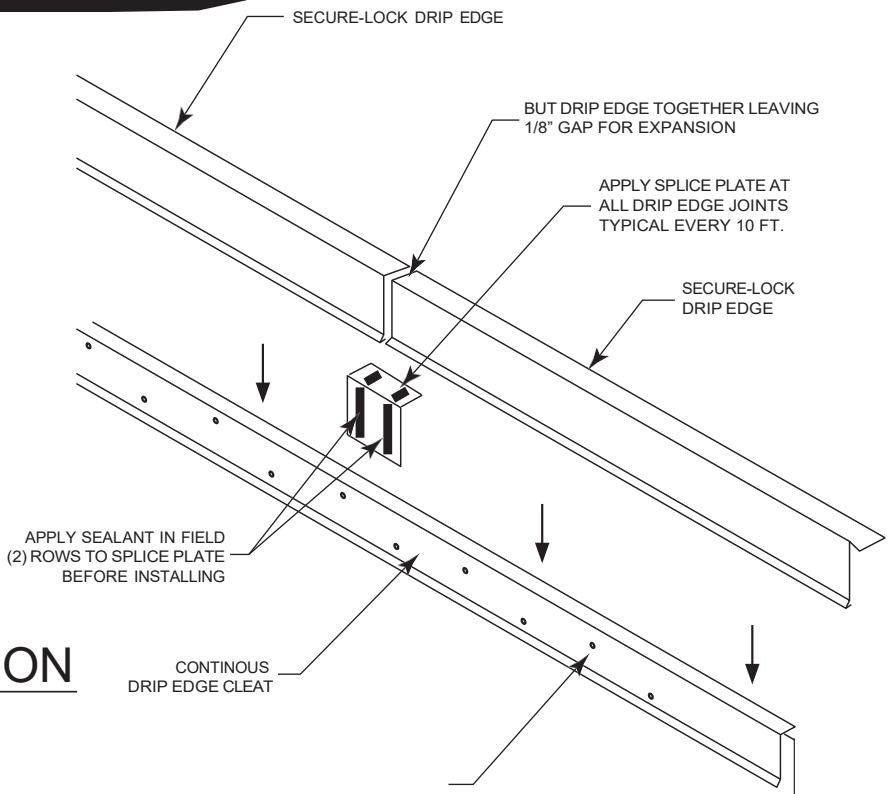


## END WALL TERMINATION

RIGHT HAND SHOWN

#10 X 1" WOOD SCREW OR 1 1/4" RING SHANK
NAIL STAGGERED @ 6" O.C., TYPICAL

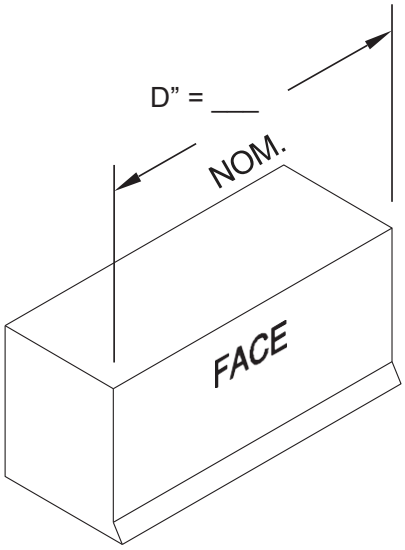


## END CAP

LEFT HAND SHOWN

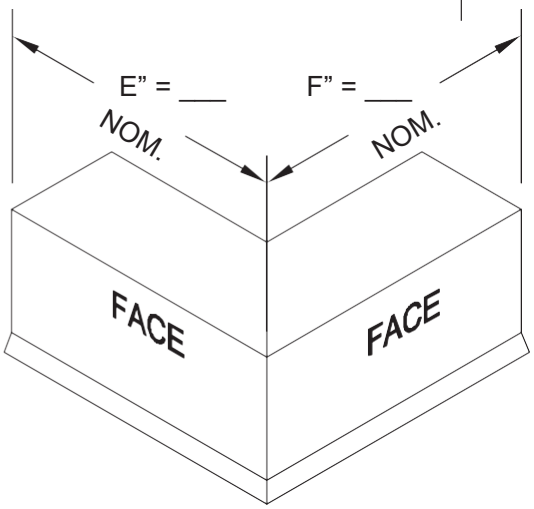


## OUTSIDE MITER

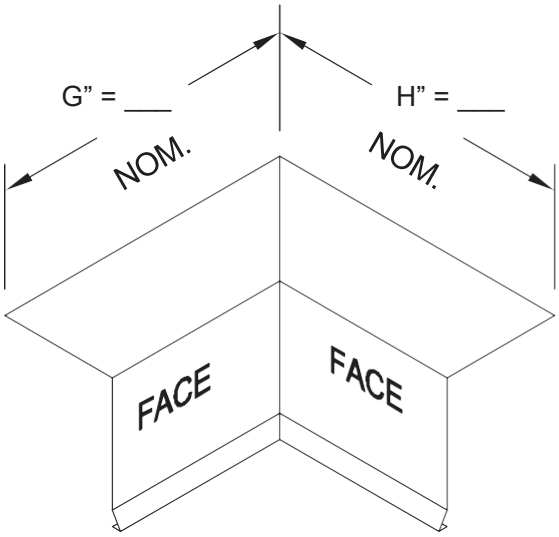


## INSIDE MITER

METAL ROOFING SYSTEMS

WWW.METALROOFINGSYSTEMS.COM
