Rapid-Lock Term Edge

METAL ROOFING SYSTEMS

WWW.METALROOFINGSYSTEMS.COM

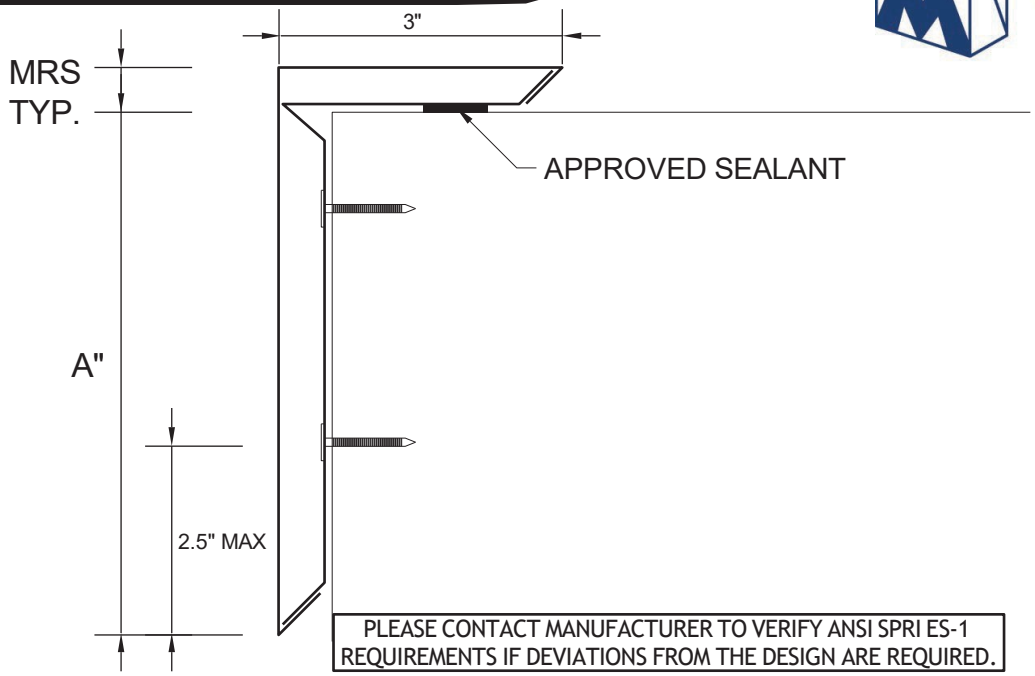

PLEASE CONTACT MANUFACTURER TO VERIFY ANSI SPRI ES-1 REQUIREMENTS IF DEVIATIONS FROM THE DESIGN ARE REQUIRED.

TERM EDGE DIMENSIONS

FRONT (A"):_____

FINISH

KYNAR (painted) ☐

COLOR: _____

MILL FINISH (unfinished aluminum) ☐

GALVALUME (unfinished steel) ☐

TERM EDGE MATERIAL

24 GAUGE GALVALUME ☐

22 GAUGE GALVALUME ☐

.032 ALUMINUM ☐

.040 ALUMINUM ☐

.050 ALUMINUM ☐

.063 ALUMINUM ☐

CLEAT MATERIAL

20 GAUGE GALVANIZED (STANDARD)

PROJECT INFORMATION

PROJECT NAME:_____

PROJECT LOCATION:_____

BUILDING HEIGHT:_____

CUSTOMER APPROVAL

ARCHITECT:_____

CUSTOMER:_____

AUTHOR SIGNATURE: _____

DATE:_____

QUANTITY

*TOTAL LINEAR FEET:_____

INSIDE MITERS:_____

OUTSIDE MITERS:_____

END CAPS LEFT:_____ RIGHT:_____

END WALL TERMINATION LEFT:_____ RIGHT:_____

NOTES

-UNLESS OTHERWISE NOTED, FABRICATION OF MITERS AND ACCESSORIES ARE FURNISHED WITH A NON-PENETRATING CLINCHED JOINT AND FACTORY APPLIED SEALANT.

-CHECK HERE IF WELDED MITERS AND ACCESSORIES ARE REQUIRED

☐ - REQUIRED (UPCHARGE)

- SYSTEM INCLUDES 6" WIDE CONCEALED SPLICE PLATES

Rapid-Lock Termination Edge

METAL ROOFING SYSTEMS

WWW.METALROOFINGSYSTEMS.COM

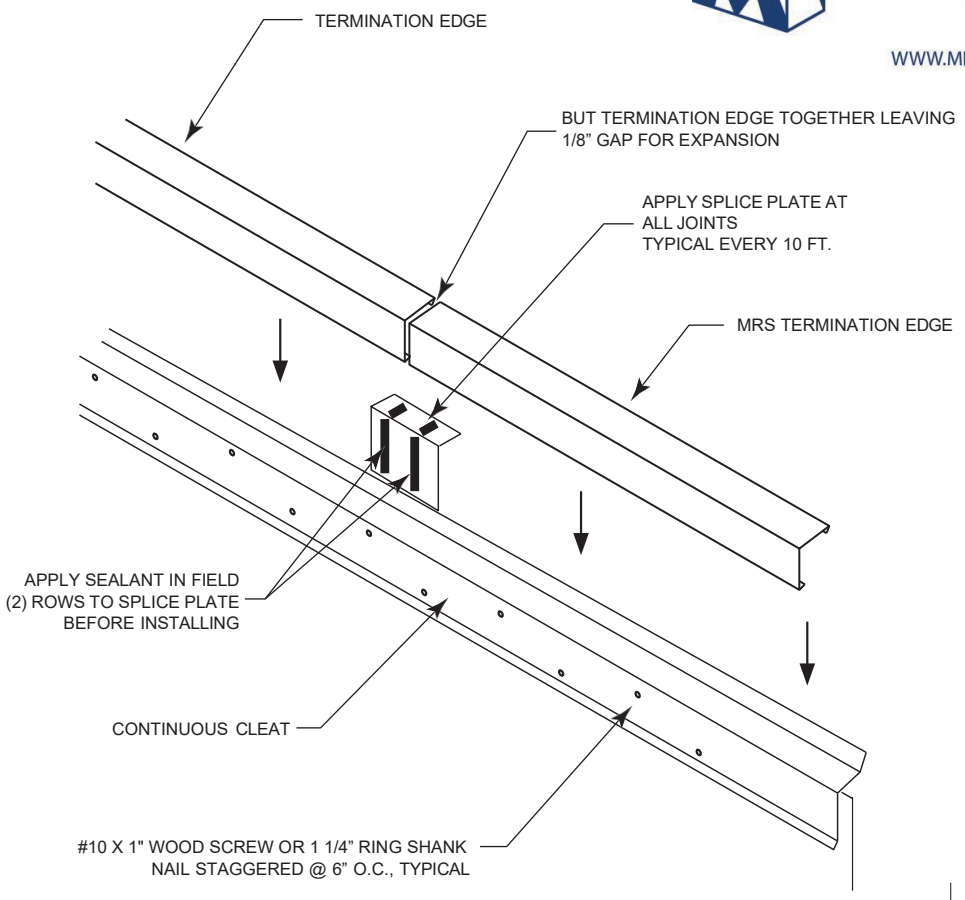

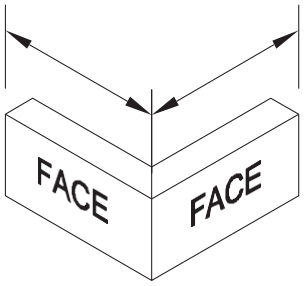

OUTSIDE MITER

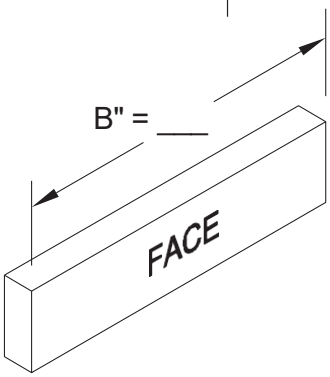

END CAP

LEFT HAND SHOWN

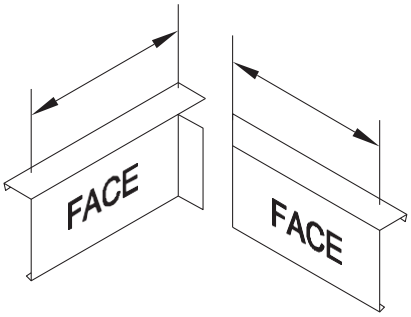

INSIDE MITER

2 PIECE ASSEMBLY

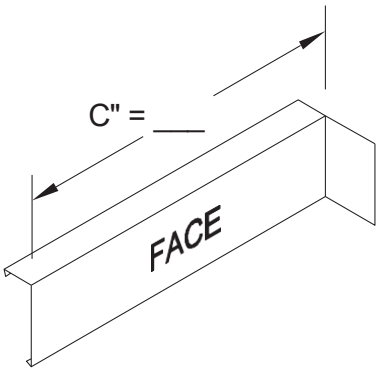

END WALL TERMINATION

RIGHT HAND SHOWN
